

+ COORDINATED WORKPLACE DECOMMISSIONING

# WORKPLACE TEARDOWN. CONTROL THE LOGISTICS. CLEAR THE WORKPLACE.

A five-day field program connected furniture teardown, staging, removal and transport preparation across a second-floor government workplace.

**5 DAYS**

FIELD PROGRAM

**CREWS**

COORDINATED REMOVAL

**ONE PLAN**

CREWS + LOGISTICS

## OVERVIEW

### CHALLENGE


The second-floor office had to be dismantled in a controlled sequence. Installers, movers, drivers, staging equipment and debris removal all had to align with restricted building removal windows and the furniture plan.

### ASI APPROACH

ASI coordinated field crews with Atlantic Relocation, separated teardown from loading, and organized furniture for transport. Equipment placement, staging and container timing were treated as part of the work, not left to the end.

### RESULTS

- Workstations dismantled and organized for transport
- Training and enclosed work areas cleared
- Crews and removal logistics sequenced together

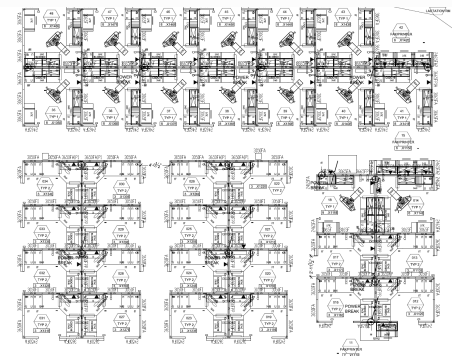

WORKSTATION TEARDOWN PLAN



WORKSTATION TEARDOWN | IN PROGRESS

## CDTFA | RANCHO CUCAMONGA

ASI delivered the teardown and staging scope for a second-floor California government office. The project required coordinated installer and moving crews, separate loading windows and dedicated transport preparation to convert the furnished workplace into cleared areas.

## PROJECT INFO

### END USER

CDTFA

### LOCATION

Rancho Cucamonga, CA

### PARTNER

Atlantic Relocation

### PROGRAM

Five field days

### DELIVERY

Teardown and logistics

### STATUS


Completed

## + PLANS AND PROJECT SCALE

# THE PLAN SET THE SEQUENCE.

## THE CREWS CONTROLLED THE FLOW.

Workstation groups and the training room made this a coordinated furniture teardown, not a series of isolated pickups. The plan linked dismantling, staging and removal across the second-floor workplace.

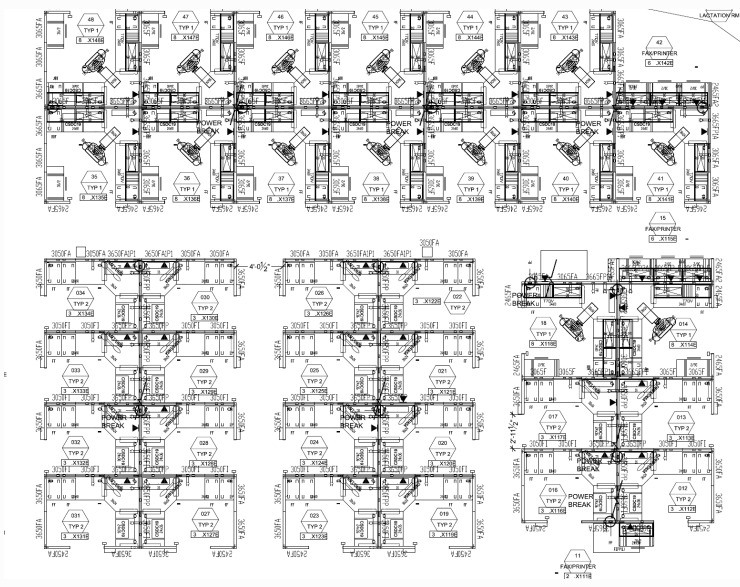

### WORKSTATION GROUPS | FURNITURE PLAN EXCERPT

## DAYS 1 + 2


FURNITURE TEARDOWN

## DAYS 3 + 4

DECOMMISSIONING + LOADING

## DAY 5

TRANSPORT ORGANIZATION

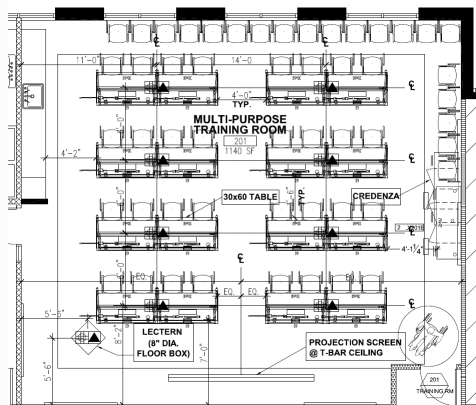

### TRAINING ROOM | FURNITURE PLAN EXCERPT

## + THE ASI DELIVERY MODEL

# THE WORK WAS MORE THAN REMOVAL.

## THE SEQUENCE MADE IT WORK.

ASI connected the furniture plan to the people, equipment and building constraints. Each stage prepared the next crew to work efficiently without losing control of materials or access.

01

### MOBILIZE THE RIGHT RESOURCES

Coordinate ASI, installer and Atlantic moving crews. Bring dollies, panel carts and protection into the building ahead of field activity.

02

### DISMANTLE BY THE PLAN

Break down cubicle groups and move components into staging, using the furnished layout to guide the teardown work.

03

### SEPARATE WORK FROM LOADING

Align daytime field activity with the building's restricted removal windows and the arrival of the moving crew.

04

### MANAGE REMOVAL LOGISTICS

Coordinate drivers, container placement and debris removal around the site's construction zones and field sequence.

05

### ORGANIZE FOR TRANSPORT

Dedicate a final crew stage to organizing dismantled furniture, connecting origin teardown to the next logistics step.

## PROJECT INFO

#### END USER

CDTFA

#### LOCATION

Rancho Cucamonga, CA

#### FLOOR

Second-floor workplace

#### FIELD PROGRAM

Five days

#### DELIVERY PARTNER

Atlantic Relocation

#### SCOPE

Teardown, staging, removal

#### STATUS

**COMPLETED**

## ONE TEAM CONTROLLED EVERY DEPENDENCY

The critical connection was between field production and material flow. Teardown, staging, loading, container service and final organization were managed as one sequence.

MOBILIZE

DISMANTLE

STAGE

LOAD

ORGANIZE

CLOSEOUT

One accountable partner from planning through final closeout.

**+ THE OUTCOME**

# A FURNISHED WORKPLACE CLEARED. A CONTROLLED TRANSITION DELIVERED.

The completed project connected a substantial furniture teardown with the practical logistics that make an office exit work: coordinated crews, organized components, removal windows and cleared work areas.

## 5 DAYS

**FIELD PROGRAM**

Four days of core field work plus transport organization.

## 2ND FLOOR

**WORKPLACE EXIT**

Workstations, training and enclosed office areas.

## ONE PLAN

**COORDINATED DELIVERY**

Installers, movers, drivers and material handling.

## WHAT THE PROJECT DELIVERED

### FURNITURE SYSTEMS DISMANTLED

Workstation teardown followed the project drawing, with components moved to staging for the next step.

### CLEARED INTERIOR AREAS

The training room and enclosed work areas were cleared following furniture removal.

### TRANSPORT PREPARATION INTEGRATED

Dedicated organization work connected the teardown scope to outbound furniture handling.

### BUILDING CONSTRAINTS INCORPORATED

Removal windows, equipment access and container placement informed the field sequence.

## ONE ACCOUNTABLE PARTNER. FROM WORKPLACE TEARDOWN TO CLOSEOUT.

**DELIVERY RESULT**

ASI completed the Rancho Cucamonga teardown, staging and transport-preparation program with Atlantic Relocation. From the first crew arrival to final organization, the office exit was managed as a connected field and logistics operation.

## PLANNING A COMPLEX OFFICE EXIT?

[ASICOINC.COM](http://ASICOINC.COM) | [INFO@ASICOINC.COM](mailto:INFO@ASICOINC.COM)




## + FIELD EXECUTION

# THE WORK IN THE FIELD.

## THE SPACE AFTER REMOVAL.


Distinct views show dismantling in progress, organized staging and completed cleared areas. The project story is the transition from assembled workplace systems to an orderly office exit.

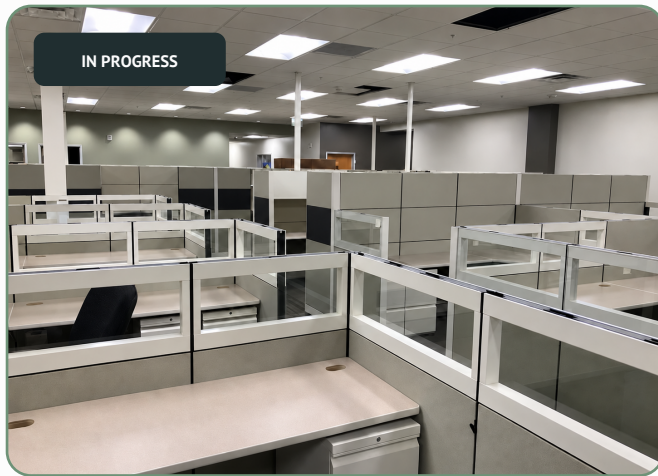

WORKSTATION TEARDOWN | IN PROGRESS



TRAINING ROOM CLEARANCE | COMPLETED

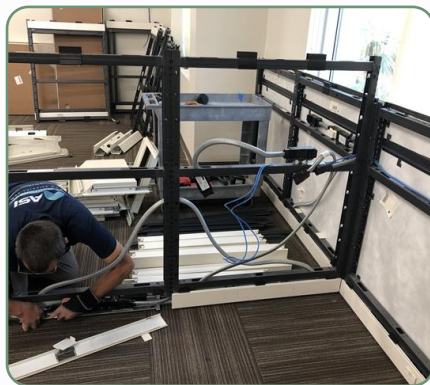

FURNITURE TEARDOWN | IN PROGRESS



TRANSPORT STAGING | IN PROGRESS



WORK AREA CLEARANCE | COMPLETED

## THE LOGISTICS ARE PART OF THE PROJECT.

Furniture teardown is only one stage of a workplace exit. ASI coordinates the crews, staging, building requirements and removal sequence so the work moves through to closeout.
