+ WORKPLACE TRANSFORMATION + INTEGRATED TRADES

59 STATIONS OUT. 64 CUBICLES IN. UNDER 48 HOURS.

A live-office transformation completed during one holiday weekend with no reported interruption to normal operations.



59	64	<48 HR
BENCHING STATIONS REMOVED	CUBICLES INSTALLED	COMPLETE TRANSFORMATION

OVERVIEW

CHALLENGE

Convert an active office from open benching to cubicles without taking the division offline or missing an unusually tight holiday-weekend deadline.

ASI APPROACH

Complete space planning, furniture sourcing, technology disconnect, clearing, power work, cubicle installation, reconnection, and verification as one integrated sequence.

RESULTS

- Transformation completed in under 48 hours
- Finished several hours ahead of schedule
- No reported interruption to normal operations

CIM GROUP

CIM Group needed a major workplace change without a lost workday. ASI connected furniture, electrical, low-voltage, and move activity into one controlled weekend plan.

PROJECT INFO

CLIENT
CIM Group

PROJECT TYPE
Weekend workplace transformation

EXISTING LAYOUT
59 benching stations

NEW LAYOUT
64 wired cubicles

WORK WINDOW
One holiday weekend

DELIVERY
Under 48 hours, several hours early

+ THE ASI APPROACH

FROM ACTIVE OFFICE TO RESET.
ONE WEEKEND PLAN.

The sequence was planned around the return-to-work deadline, with each trade and handoff positioned to keep the next activity moving.

01

PREPLAN

Confirm the layout, furniture package, power path, cabling sequence, crews, access, protection, and handoffs.

02

DISCONNECT

Protect equipment, disconnect computers, remove cabling, and prepare the active work area for change.

03

CLEAR

Remove 59 benching stations and clear the floor for power and furniture installation.

04

INSTALL

Set power conduits, erect cubicle walls and desks, and complete the new 64-station layout.

05

RECONNECT

Restore electrical and technology connections, verify the finished condition, and release the space.

PROJECT INFO

STARTING POINT
59 benching stations

COMPLETED LAYOUT
64 cubicles

SCHEDULE
Under 48 hours

FINISH
Several hours early

WORK WINDOW
Holiday weekend

OPERATIONS
No reported interruption

WORKDAYS LOST
ZERO REPORTED

DESIGNED AROUND MONDAY MORNING

The deadline shaped every decision. Space planning, disconnects, material movement, power, furniture, reconnection, and quality control were sequenced backward from the return-to-work requirement.

The integrated plan removed the need for separate client coordination across trades and created one clear owner for the finished workplace.

+ THE OUTCOME

64 WIRED CUBICLES.
READY BEFORE THE DEADLINE.

The office moved from open benching to a complete cubicle environment in less than two days.

59

STATIONS REMOVED

The existing benching layout was cleared during the weekend window.

64

CUBICLES INSTALLED

Furniture, power, and technology were delivered as one new layout.

<48 HR

TOTAL EXECUTION

The team finished several hours before the required handoff.

WHAT THE PROJECT DELIVERED

INTEGRATED TRADES

Furniture, electrical, technology, space planning, and move activity were managed through one delivery plan.

WORKPLACE CONTINUITY

The holiday-weekend sequence avoided a reported interruption to normal office operations.

SCHEDULE CONFIDENCE

Crews completed the transformation several hours ahead of the committed deadline.

PURPOSE-BUILT LAYOUT

Low partitions preserved connection while giving employees more defined personal workspace.

ONE ACCOUNTABLE PARTNER. NATIONWIDE.
FROM PLAN TO CLOSEOUT.

PROJECT NOTE

The full transformation was completed during one holiday weekend, several hours ahead of the required handoff, with no reported interruption to normal operations.

READY TO MOVE YOUR PROJECT FROM PLAN TO FIELD?

ASICOINC.COM | INFO@ASICOINC.COM

+ WEEKEND TRANSFORMATION

BENCHING OUT. CUBICLES IN.
LESS THAN TWO DAYS.

The project moved from the existing layout through active installation to a completed cubicle environment.



BEFORE

The starting condition was documented and cleared within the weekend sequence.




IN PROGRESS

Crews coordinated furniture, cabling, and workstation assembly in one controlled flow.

COMPLETED

The new 64-station layout was finished and ready before the required handoff.

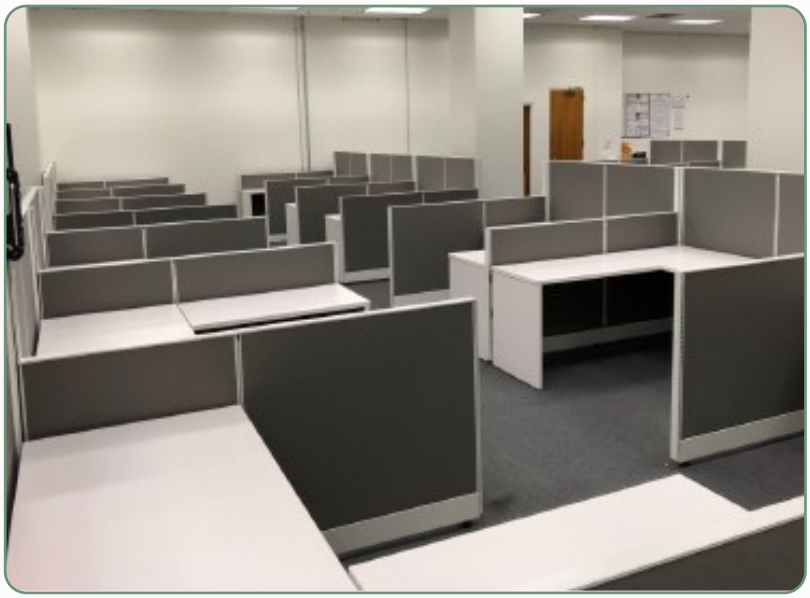

+ CLIENT PERSPECTIVE

A TIGHT DEADLINE.
A TRUE WORKING PARTNERSHIP.

The client relationship and integrated field plan gave the team room to move quickly without losing control of the outcome.



> Right from the beginning, ASI made it very clear that they were here to work with us, not for us.

Mary Rainwater, Director, Administrative and Office Services, CIM Group

WHY IT WORKED

PREPLANNED SEQUENCE

Every disconnect, removal, installation, and reconnection had a defined place in the weekend plan.

SINGLE ACCOUNTABILITY

ASI connected the trades and decisions through one project-management layer.

VERIFIED HANDOFF

The completed layout was ready several hours before employees returned.

ONE ACCOUNTABLE PARTNER FROM PLANNING THROUGH FINAL CLOSEOUT.

ASI coordinates workplace planning, furniture, electrical, low-voltage, move activity, and final closeout through one accountable team.

ASICOINC.COM | INFO@ASICOINC.COM
